



অসম চৰকাৰ
অসম আভ্যন্তৰীণ জল পৰিবহন উন্নয়ন সমিতি

Government of Assam

Assam Inland Water Transport Development Society

3rd floor, Directorate of Inland Water Transport, Ulubari, Guwahati- 7::email: dir.iwtas-as@gov.in::Tel:+91361-2526421

No. AIWTDS/189/2019/.....³⁷⁸

Date: ..^{12th} Aug'2021

Corrigendum No -I

In reference to the tender notification no. **AIWTDS/189/2019/323** dated 22.07.2021 for E-procurement of "Appointment of Technical Services and Supervision Consultant (TSSC) firm for providing consulting services for Construction of terminal and riverine infrastructure at **Guwahati Gateway Ghat (GGG)**, Assam", certain amendments enclosed as Annexure-I, reply to pre-bid queries as Annexure -II and concept plan as Annexure-III which will be the part of the issued document. Consultants/Bidders are requested to take the note of these amendments prior to the submission of bid/ proposal. The last date for submission of bid is extended and the new date for online bid submission is 26.08.2021 at 1400 hrs.

Deputy State Project Director

Assam Inland Water Transport Development Society

Memo No. AIWTDS/189/2019/~~323~~³⁷⁸A

Dated:..^{12th} August,2021

Copy to:

Memo No.

Copy to: i) The Director, IWT Assam for information and also for publishing the Corrigendum-I on the website of DIWT www.iwtdirectorate.assam.gov.in

ii) Web Portal of Assam IWTD Society iii) e-procurement portal of Govt. of Assam viz. www.assamtenders.gov.in

Deputy State Project Director

Assam Inland Water Transport Development Society

372

Corrigendum No. I -Annexure I

RFP No: IN-IWT-236184-CS-QCBS dated 22/07/2021

Project: "Appointment of Technical Services and Supervision Consultant (TSSC) firm for providing consulting services for Construction of terminal and riverine infrastructure at Guwahati Gateway Ghat (GGG), Assam"

Existing		Modified/ to be read as									
Sl No	Clause Reference										
1.	Phase 3 7.8 Defects Liability Period	The time schedule for the construction activities of the Guwahati Gateway Ghat has been proposed as 18 months after the award of contract. However for TSSC, the project duration considered as 30 Months which includes bid process management prior to award of contractor									
2.	ITB/ BDS 14.1.2	Estimated input of Key Experts' time-input: 255 person-months.									
3.	SCC 41.2 Payment Schedule	<p>The payment schedule:</p> <p>The payment under this assignment shall be made, after due acceptance of the deliverables by the society, as per the milestones detailed below:</p> <table><tr><th>Sl No</th><th>Milestone</th><th>Percentage</th></tr><tr><td>1</td><td>On Acceptance of Bid Process Management Report</td><td>2.5% of contract Value</td></tr><tr><td>2</td><td>On Acceptance of Inception Report</td><td>2.5% of contract Value</td></tr></table>	Sl No	Milestone	Percentage	1	On Acceptance of Bid Process Management Report	2.5% of contract Value	2	On Acceptance of Inception Report	2.5% of contract Value
Sl No	Milestone	Percentage									
1	On Acceptance of Bid Process Management Report	2.5% of contract Value									
2	On Acceptance of Inception Report	2.5% of contract Value									

SI No	Clause Reference	Existing		Modified/ to be read as	
	1	On Acceptance of Bid Process Management Report	2.5% of contract Value	3	On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other submissions, test report audit report, compliance report, certificate, plan, manual and any other deliverable mentioned in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts.
	2	On Acceptance of Inception Report	2.5% of contract Value		
	3	On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other submissions, test report audit report, compliance report, certificate, plan, manual and any other deliverable mentioned in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts.	8.5% of Contract Value per quarter.		
				4	
					On Acceptance of Final Completion report with CD
					10% of Contract Value.

378

Existing		Modified/ to be read as
Sl No	Clause Reference	
4	On Acceptance of Final Completion report with CD	10% of Contract Value per quarter.
4.	ITB/BDS 6.3 Joint Venture	Eligibility As an exception to the fore going ITC 6.1 and ITC 6.2 above: Joint Venture, association with other firms and engagement of Sub-consultant is not allowed.
5.	Team Leader cum Project Management Expert	Educational Qualification Should be a Graduate in Civil Engineering. Post-Graduation in Project Management / Port /Marine Engineering will be preferred. Minimum 20 years of overall experience, including 5 years of experience as Team Leader in Port/IWT related construction supervision and Project management.
		Eligibility ITB 6.3 is deleted in totality. Proposal may be submitted as a Consortium/ JV of maximum of 2 Firms including the Lead Member. If the proposal is being submitted as Consortium/JV, the proposal shall consist of a Consortium Agreement signed by both the parties clearly mentioning the division of scope of work, composition of team members of both the parties.
		To be read as Educational Qualification Should be a Graduate in Civil Engineering. Post-Graduation in Civil Engineering/ Ocean Engineering / Port /Marine Engineering will be preferred. Certification in Project Management from PMI/RICS/Prince 2 shall be desirable.

Sl No	Clause Reference	Existing	Modified/ to be read as
			<p>Minimum 20 years of overall experience, including 5 years of experience as Team Leader in Port/IWT related construction supervision and Project management.</p>
6.	<p>Resident Engineer cum Construction Expert to be based at Site Full time</p>	<p>Educational Qualification</p> <p>Should be a Graduate in Civil Engineering. Post-Graduation in Project Management/ Port /Marine Engineering will be preferred.</p>	<p>To be read as</p> <p>Educational Qualification</p> <p>Should be a Graduate in Civil Engineering. Post-Graduation in Civil Engineering/ Ocean Engineering / Port /Marine Engineering/ Construction Management will be preferred.</p>
		<p>Minimum 15 years of overall experience including 5 years of experience in Port/IWT related constructions works / project management installation of large diameter driven and/or bored RCC piles or steel tubular piles or precast concrete piles of large lengths in marine/riverine conditions.</p>	<p>Minimum 15 years of overall experience including 5 years of experience in Port/IWT related constructions works / construction management installation of large diameter driven and/or bored RCC piles or steel tubular piles or precast concrete piles of large lengths in marine/riverine conditions.</p>
7.	<p>MIS Expert</p>	<p>Educational Qualification</p> <p>Should be a Graduate in computer Science. Master's degree in Construction Management from a reputed and recognized university or institution shall be preferred</p>	<p>To be read as</p> <p>Educational Qualification</p> <p>Should be a BE in Computer Science/ MCA/ Master's Degree in Information Technology from a reputed institution.</p> <p>Minimum 7 years of experience of working with Management Information System for Private / Public sector / Government organizations and</p>

SI No	Clause Reference	Existing	Modified/ to be read as			
		Minimum 7 years of experience of working with Management Information System for Private / Public sector / Government organizations and specifically more than 5 years of experience in MIS implementation and Project management for large Infrastructure programs.	specifically more than 5 years of experience in MIS implementation and Project management for large Infrastructure project.			
8.	Section 7- ToR 11. Qualification & Experience of Key Personnel	SI no 8 Environmental Specialist	Add the below mentioned			
Position		Educational Qualification		Experience, Roles & Responsibility		
Environmental Specialist		Post graduate qualification in environmental engineering/ environmental science or related field		1. Experience of at least 10 years in supervision of environmental aspects of infrastructure, including water facing infrastructure 2. Will be responsible for ensuring the implementation of environmental provisions of the ESMP 3. Will advise the stakeholders, including TSSC team leader, resident engineer, and if appropriate contractor personnel on steps to be taken to manage anticipated impacts		

9/12

Existing		Modified/ to be read as				
SI No	Clause Reference			4. Monitor and report on the Contractor's management of environmental aspects		
				If any shortcomings are noticed, will advise on rectification steps, and if these persist, will advise TTL on effective next steps to prevent unacceptable damage due to such shortcomings, including accidents		
9.	Section 7- ToR	SI no 9 Social Development Specialist	Add the below mentioned			
11. Qualification & Experience of Key Personnel			Position	Educational Qualification	Experience, Roles &	
			Social Development Specialist	Postgraduate in Sociology / Social Work or relevant disciplines.	1.Ensure worksite is free of encumbrances and requirements of RAP are met prior to construction activities. 2.Review and finalize contractor's ESMP, including contractor's Code of Conduct, Labor Influx/ Workers Camp Management Plan, and other Plans prepared by the contractor. 3.Monitor and report on contractor's adherence to approved plans. In case of non-compliance, consultant to	
				Minimum 10 years of experience in the relevant field.		

392601

Sl No	Clause Reference	Existing	Modified/ to be read as		
					correct/rectify the issue as per the safeguard requirements. Ensure all construction related grievances are addressed in a timely manner.
10.	ITB/BDS 10.1	<p>The Proposal shall comprise the following: For FULL TECHNICAL PROPOSAL (FTP): Technical Proposal to be uploaded in the "Technical Folder" available in the e-procurement portal:</p> <p>(1) Power of Attorney to sign the Proposal</p> <p>(2) TECH-1</p> <p>(3) TECH-2</p> <p>(4) TECH-3</p> <p>(5) TECH-4</p> <p>(6) TECH-5</p> <p>(7) TECH-6</p> <p>(8) TECH-7 Code of Conduct (ESHS) [The Consultant shall submit the Code of Conduct that will apply to the Consultant's Key Experts and Non-Key Experts, to ensure compliance with good Environmental, Social, Health and Safety (ESHS) practice. In addition, the Consultant shall submit an outline of how this Code of Conduct will be implemented. The successful Consultant shall be required to implement the agreed Code of Conduct upon contract award.]</p>	<p>The referred Clause is to be read as mentioned below:</p> <p>The Proposal shall comprise the following: For FULL TECHNICAL PROPOSAL (FTP): Technical Proposal to be uploaded in the "Technical Folder" available in the e-procurement portal:</p> <p>(1) Power of Attorney to sign the Proposal</p> <p>(2) TECH-1</p> <p>(3) TECH-2</p> <p>(4) TECH-3</p> <p>(5) TECH-4</p> <p>(6) TECH-5</p> <p>(7) TECH-6</p> <p>(8) TECH-7 Code of Conduct (ESHS) [The Consultant shall submit the Code of Conduct that will apply to the Consultant's Key Experts and Non-Key Experts, to ensure compliance with good Environmental, Social, Health and Safety (ESHS) practice. In addition, the Consultant shall submit an outline of how this Code of Conduct will be implemented. The successful Consultant shall be required to implement the agreed Code of Conduct upon contract award.]</p> <p>(9) State of Undertaking</p> <p>AND Financial Proposal: To Be Submitted in the FINANCIAL FOLDER available in the e-procurement portal under the RFP:</p> <p>(1) FIN-1</p> <p>(2) FIN-2</p> <p>(3) FIN-3</p>		

	<p>AND Financial Proposal: To Be Submitted in the FINANCIAL FOLDER available in the e-procurement portal under the RFP:</p> <p>(1) FIN-1 (2) FIN-2 (3) FIN-3 (4) FIN-4</p> <p>(5) Statement of Undertaking (if required under Data Sheet 10.2 below)(ALL FIN FORMS SHALL BE SUBMITTED IN THE FINANCIAL FOLDER ONLY. PROPOSAL SHALL BE SUMMARILY REJECTED IN CASE BIDDER SUBMIT ANY PRICE INFORMATION OTHER THEN FINACIAL FOLDER)</p>	<p>(ALL FIN FORMS SHALL BE SUBMITTED IN THE FINANCIAL FOLDER ONLY. PROPOSAL SHALL BE SUMMARILY REJECTED IN CASE BIDDER SUBMIT ANY PRICE INFORMATION OTHER THEN FINACIAL FOLDER)</p>
11	<p>Section 2 - Instructions to Consultants (ITC)</p> <p>Data Sheet - Clause 17.7 and 17.9 on page 44 of the RFP The Proposals must be submitted no later than: Date: 17th Aug, 2021 Time: 14:00 hours IST</p>	<p>Data Sheet - Clause 17.7 and 17.9 on page 44 of the RFP The Proposals must be submitted no later than: Date: 26th August, 2021 Time: 14:00 hours IST</p>



Deputy State Project Director

Assam Inland Water Transport Development Society

Reply to Pre-Bid Queries- Annexure- II

RFP No: IN-IWT-236184-CS-QCBS dated 22/07/2021

Project: "Appointment of Technical Services and Supervision Consultant (TSSC) firm for providing consulting services for Construction of terminal and riverine infrastructure at Guwahati Gateway Ghat (GGG), Assam"

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
1.	E. Data Sheet, Page no.37 of RFP	Estimated input of Key Experts' time-input: 68person-months.	We presume that proposed man-months are indicative only and consultant can propose required number of man-months. Please clarify whether our interpretation is correct or not	Refer Corrigendum I- Sl no 2
2.	Clause 21.1, S.no.3,	The firm should have completed in last 5 years atleast 5(five) similar technical support consultancyservices in any sector out of which: 1(one) should be in the water/marine sector . 1(one) should be externally aided project in India.	We presume that water sector means any feasibility study, DPR for water supply sector in urban areas will be considered. Please clarify whether our interpretation is correct or not.	Water sector is Inland Water Transport/ Marine/ Port.
3.	Clause 21.1, S.no.4,	The firm should have experiences in last 5 years in providing technical support Service for at least 1 activities involving construction of : 1. Jetty in river/sea or a bridge in river. And 2. Civil works of Jetty/bridge involving minimum 1200 mm diameter or equivalent area piles in marine / river conditions.	The consultant has completed Design Projects of a Jetty in River/sea but construction activity was not part of scope of work of consultant. We presume that Design Projects of Jetty also consider for evaluation. Please clarify whether our interpretation is correct or not.	No Changes
4.	Part B: iv.	Minimum of 1 nos. technical support service for activities involving	We also request you to please allow construction supervision projects related to railway and road sectors. The consultant has completed Design Projects of a Jetty in River/sea but	No Changes

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
		construction of (executed in the last 5 years): 1. Jetty in river/sea or a bridge in river. And 2. Civil works of Jetty/bridge involving minimum 1200 mm diameter or equivalent area piles in marine / river conditions. : 1 point For each additional assignment executed in the last 5 years : 1 point for each additional assignment subject to maximum of three (03) assignment.	constriction activity was not part of scope of work of consultant. We presume that Design Projects of Jetty also consider for evaluation. Please clarify whether our interpretation is correct or not. We also request you to please allow construction supervision projects related to railway and road sectors.	
5.	Section 7: TOR 11. Qualification Experience of Key Personnel;	Table showing list of Key Resource's, Non-Key Resources and Support staffs to be based at site full time. <ul style="list-style-type: none"> • Environmental Specialist – 18 Man Months • Social Development Specialist– 18 Man Months 	There is some changes between the Table showing list of key experts and Clause 11. Qualification & Experience of Key Personnel; Because Environmental Specialist and Social Development Specialist related educational qualification, experience, roles and responsibilities are missing under Clause 11. Qualification & Experience of Key Personnel. We presume that Environmental Specialist and Social Development Specialists are not required for the project. Please clarify whether our interpretation is correct or not.	Refer Corrigendum I, Sl no 8 & 9
6.	Clause 11. Qualification Experience of Key Personnel;	Team Leader cum Project Management Expert - Post-Graduation in Project Management / Port /Marine Engineering will be preferred.	There is no specialization in Port / Marine Engineering but M. Tech offered by R.E.C, Surathkal (Specialization in Marine Structures), Karnataka is the most eligible/appropriate Master Degree for Ports / Marine Sector Experts in India. The curriculum has all the facets related	Refer Corrigendum I, Sl no 5

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
			to Port planning, port engineering, design of port / marine structures and its related land side infrastructure developments. We presume that M. Tech with specialization in Marine Structures will be Considered as equivalent to Post-Graduation in Port /Marine Engineering. Please clarify whether our interpretation is correct or not.	
7.	Clause 11. Qualification & Experience of Key Personnel	Resident Engineer cum Construction Expert to be based at Site Full time - Post-Graduation in Project Management / Port /Marine Engineering will be preferred.	There is no specialization in Port / Marine Engineering but M. Tech offered by R.E.C, Surathkal (Specialization in Marine Structures), Karnataka is the most eligible/appropriate Master Degree for Ports / Marine Sector Experts in India. The curriculum has all the facets related to Port planning, port engineering, design of port / marine structures and its related land side infrastructure developments. We presume that M. Tech with specialization in Marine Structures will be Considered as equivalent to Post-Graduation in Port /Marine Engineering. Please clarify whether our interpretation is correct or not.	Refer Corrigendum I, Sl no 6
8.	Clause 11. Qualification & Experience of Key Personnel	Sr. Structural Engineer- Graduate in Civil Engineering. Higher qualifications and specialization in port related civil designs will be preferred.	There is no specialization in Port related Civil Designs but M. Tech offered by R.E.C, Surathkal (Specialization in Marine Structures), Karnataka is the most eligible/appropriate Master	No changes

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
			Degree for Ports / Marine Sector Experts in India. The curriculum has all the facets related to Port planning, port engineering, design of port / marine structures and its related land side infrastructure developments. We presume that M. Tech with specialization in Marine Structures will be Considered as equivalent to Post-Graduation in Port /Marine Engineering. Please clarify whether our interpretation is correct or not	
9.	Clause 11. Qualification & Experience of Key Personnel;	Sr. Mechanical Engineer/ Marine Engineer - Graduate in Mechanical / Marine Engineering.	There is no specialization in Marine Engineering but M. Tech offered by R.E.C, Surathkal (Specialization in Marine Structures), Karnataka is the most eligible/appropriate Master Degree for Ports / Marine Sector Experts in India. The curriculum has all the facets related to Port planning, port engineering, design of port / marine structures and its related land side infrastructure developments. We presume that M. Tech with specialization in Marine Structures will be Considered as equivalent to Post-Graduation in Port /Marine Engineering. Please clarify whether our interpretation is correct or not.	No Changes
10.	Clause 11. Qualification & Experience of Key Personnel;	MIS Expert - Graduate in computer Science. Master's degree in Construction Management.	We also request the Client to please allow Graduate in Computer Science and Master's Degree in IT, Computer	Refer Corrigendum I, Sl no 7

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
11.	Clause 41.2 - The payment schedule:	<ul style="list-style-type: none"> On Acceptance of Bid Process Management Report – 2.5% of Contract Value On Acceptance of Inception Report– 2.5% of Contract Value On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other submissions, test report audit report, compliance report, certificate, plan, manual and any other deliverable mentioned in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts– 8.5% of Contract Value per quarter. On Acceptance of Final Completion report with CD - 10% of Contract Value per quarter. 	<p>Science also equal qualification for MIS Expert.</p> <p>Payments are not matching with 100% hence kindly review and also include 20% towards mobilization advance.</p>	Refer Corrigendum I, Sl no 3
12.	Section 7, Pg 79	Section 7 - Terms of Reference	Please provide us the information pertaining to the proposed infrastructure to the consultant along with a layout so that one can estimate the efforts required for the project.	The suggestive concept plan is attached as Annexure-III.

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
13.	RfP	RfP	In case the contractor delays the project beyond the contract of TSSC consultant, we expect AIWT to extend the duration of the consultant's contract on mutually agreed rates. Please confirm.	Kindly refer to Contract form in the RfP document.
14.	Section 7, Point 9, Page 99 & 100	Data, services, and facilities to be provided by the employer The following and any other such data, available with the AIWTDS shall be provided to the TSSC: models of past RFQ, RFP, project details, specifications, designs (as and when required) and Schedules or any other relevant document supportive to project development prepared by AIWTDS.	As per standard industry practice, normally the Contractor's team provides such facilities (office, cars, etc) to the Consultant's team. Please confirm.	Kindly refer to the Clause no ITB/BDS 16.1
15.	Page 113	Standard Form of Contract Consultant's Services Lump-Sum	The model form of contract given in the RfP applies to Lump-Sum contracts. Since this is PMC job, we kindly request you to make monthly payment as per the deployment of staff on actuals.	No Changes in the documents
16.		RfP – Submission date of proposal	We understand your urgency for appointment of consultant at the earliest, however we kindly request you to grant atleast 1 week extension of time for submission of proposal. We will require this time to make a compliant bid and quality submission.	Kindly refer Corrigendum I, Sl no 11.

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
17.	Invitation Proposals	Point h <ul style="list-style-type: none"> “One of the important tasks of the Consultants shall be to verify whether the pre-construction tasks and statutory/regulatory clearances are completed prior to the handing over of the encumbrance free site areas to the Contractors for initiating construction work- For instance compensation payment to the affected people shall be completed prior to begin civil work.” 	1) May request AIWTDS to kindly conform that, TSSC scope comprises to review and provide technical assistance in statutory/regulatory clearances required for the project implementation. TSSC is not responsible for obtaining the statutory/regulatory clearances 2) May also request AIWTDS to clarify the impact of TSSC project duration in case the project execution is delayed due to statutory/regulatory clearances, etc.	TSSC to facilitate and provide technical assistance of the required statutory/regulatory clearances required for the project implementation. Kindly refer the provisions of the Contract.
18.	Section 2 - Instructions to Consultants (ITC)	Point m. “Joint Venture (JV)” means an association with or without a legal personality distinct from that of its members, of more than one Consultant where one member has the authority to conduct all business for and on behalf of any and all the members of the JV, and where the members of the JV are jointly and severally liable to the Client for the performance of the Contract. <ul style="list-style-type: none"> “Similar assignment” is defined as consultancy works carried out for technical support service. 	We request the client to clarify the “Number of members in a consortium to form a JV”. Further, we request the client to allow “Indian companies to use their Parent / Group company credentials for fulfilling the relevant experience as mentioned in clause 21.1, point 3 and 4 on page 40 of the RFP, without the parent /group company being a part of the consortium. However, an undertaking to this effect shall be provided to the client for use of such credentials.	Kindly refer Corrigendum I, Sl no 4. The Bidder may use the credentials of parent/group company if the Bidder is 100% immediate subsidiary of the parent/group company. The shareholding pattern is to be certified by the Company Secretary of the Bidder.

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
			May request AIW/TDS to kindly consider the consultancy works carried out for Construction supervision, Independent Engineer's services, PMC services, Third Party Inspection in any infrastructure sector should be considered as Similar assignments.	If the scope of the work is similar to the requirement of the ToR, Bidder to provide an extract of the agreement/ certificate from the Client as a proof of claiming eligibility.
			We understand under Technical Support Service, the client shall consider the experience of the consultant in which preparation of DPR / PMC / TPQA etc shall be considered as the scope pertains to providing technical and engineering support for such projects.	The credentials DPR/PMC shall be considered if the scope of work is similar to the ToR.
19.	Section 2 - Instructions to Consultants (ITC)	Data Sheet - on page 44 of the RFP <ul style="list-style-type: none"> Point 3) Relevant experience in the North East Region (working level fluency in local language(s)/knowledge of local culture or administrative system, government organization, etc.): 10% 	We request the client to delete the 10% weightage allowed to experts for experience in North East region and allow the same weightage for experts having experience PAN India overall.	No Change in the document
20.	Section 2 - Instructions to Consultants (ITC)	Data Sheet - Clause 17.7 and 17.9 on page 44 of the RFP <ul style="list-style-type: none"> The Proposals must be submitted no later than: Date: 17th 	We request the client to extend the proposal due date by atleast 3 weeks from the date of issue of prebid clarifications.	Kindly refer Corrigendum I, SI no 11.

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
		Auygust,2021 Time:14:00 hours IST		
21.	Section 7. Terms of Reference	Clause 6.1.1 on page 83 of the RFP Project Completion Time: Estimated Project Completion time is 24months Clause 14.1 - Section 8. Conditions of Contract and Contract Forms (Lump- Sum) • The time period shall be Thirty (30) months from the commencement of services.	We request the client to please clarify the project duration.	Kindly refer Corrigendum I, Sl no 1
22.	Section 7. ToR Clause 7, Page 83	• The Project comprises of terminals and riverine infrastructure at Guwahati Gateway Ghat (GGG) and the construction works are likely to commence in July 2021.	May request AIWTDs to kindly detail the present status of project and the status of selection of constructors for construction works considering the TSSC scope also includes Bid Process Management phase.	The RFP documents for the Construction of the Terminal is expected to be published before the Proposal due Date of TSSC.
23.	Section 7. ToR Clause 7.2.3, Page 85	• TSSC shall be responsible for review and finalization of detailed engineering designs, drawings and other technical document submission made by the Contractor to ensure compliance with applicable guidelines, standards, local rules and regulations, WB guidelines	May request AIWTDs to kindly confirm that, TSSC shall only review and suggest any corrections required in detailed engineering designs, drawings and other technical documents submitted by Contractor. The Contractor shall be responsible for making corrections and finalizing the detailed engineering designs, drawings and other technical documents.	TSSC shall review, comment and approve the submissions of the Contractor. Kindly refer ToR.

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion																				
24.	Section 7. ToR Clause 7.5.1, Page 90	(iii) Check & approve sources of materials and ask the Contractor to submit materials ordering schedule; and Employers rules and regulations	May request AIWTDS to kindly confirm, that the cost to be incurred in checking & approving the sources of materials for construction works shall be reimbursed by AIWTDS as per actuals, as the same cannot be estimated and added in the Financial proposal at this stage of proposal submission.	In case of checking & approving the source of materials from outside the North Eastern States of India shall be arranged by AIWTDS.																				
25.	Section 7. ToR Clause 10, Page 100	<table><thead><tr><th>Resource</th><th>Manmonths</th></tr></thead><tbody><tr><td>Sr. Quality Assurance cum Material Engineer</td><td>8</td></tr><tr><td>Sr. Electrical Engineer</td><td>8</td></tr><tr><td>Sr. Mechanical Engineer (Including Defect Liability Period)</td><td>8</td></tr><tr><td>Contract Specialist & Commercial manager</td><td>6</td></tr></tbody></table>	Resource	Manmonths	Sr. Quality Assurance cum Material Engineer	8	Sr. Electrical Engineer	8	Sr. Mechanical Engineer (Including Defect Liability Period)	8	Contract Specialist & Commercial manager	6	May request AIWTDS to kindly increase the required Manmonths for some of the Key experts as below, considering the TSSC scope of works. <table><thead><tr><th>Resource</th><th>Manmonths</th></tr></thead><tbody><tr><td>Sr. Quality Assurance cum Material Engineer</td><td>24</td></tr><tr><td>Sr. Electrical Engineer</td><td>12</td></tr><tr><td>Sr. Mechanical Engineer (Including Defect Liability Period)</td><td>16</td></tr><tr><td>Contract Specialist &</td><td>10</td></tr></tbody></table>	Resource	Manmonths	Sr. Quality Assurance cum Material Engineer	24	Sr. Electrical Engineer	12	Sr. Mechanical Engineer (Including Defect Liability Period)	16	Contract Specialist &	10	No Changes in the document
Resource	Manmonths																							
Sr. Quality Assurance cum Material Engineer	8																							
Sr. Electrical Engineer	8																							
Sr. Mechanical Engineer (Including Defect Liability Period)	8																							
Contract Specialist & Commercial manager	6																							
Resource	Manmonths																							
Sr. Quality Assurance cum Material Engineer	24																							
Sr. Electrical Engineer	12																							
Sr. Mechanical Engineer (Including Defect Liability Period)	16																							
Contract Specialist &	10																							

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion		Reply to Query/ Clarification/ Suggestion
			Commercial manager		
26.	Section 7. ToR Clause 11, Page 101	Qualification & Experience of Key Personnel Team Leader cum Project Management Expert: <ul style="list-style-type: none"> Should be a Graduate in Civil Engineering. Post-Graduation in Project Management / Port /Marine Engineering will be preferred. 	May request AIWTDS to also include Post Graduation in Civil Engineering/ Ocean Engineering as the preferred minimum educational qualification for the Expert "Team Leader cum Project Management Expert".		Kindly refer Corrigendum I, Sl no 5
27.	Section 7. ToR Clause 11, Page 101	Qualification & Experience of Key Personnel Resident Engineer cum Construction Expert to be based at Site Full time: <ul style="list-style-type: none"> Should be a Graduate in Civil Engineering. Post-Graduation in Project Management / Port /Marine Engineering will be preferred. 	May request AIWTDS to also include Post Graduation in Civil Engineering/ Ocean Engineering as the preferred minimum educational qualification for the Expert "Team Leader cum Project Management Expert".		Kindly refer Corrigendum I, Sl no 6
28.	Section II. GCC Clause 41.2.2, Page 137	<ul style="list-style-type: none"> The Lump-Sum Installment Payments. The Client shall pay the Consultant within sixty (60) days after the receipt by the Client of the deliverable(s) and the cover invoice for the related lump-sum installment payment. 	May request AIWTDS to kindly reduce the Lump sum installment payment schedule to the Consultant from sixty (60) days to 30 (days), considering the monthly expenses to be borne by the Consultant in deployment and site establishment.		No changes in the document

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
29.	Section III. SCC Clause 41.2, Page 145	Payment Schedule	May request AIW/TDS to kindly to modify the payment schedule as below, in reference to the TSSC scope of services.	Kindly refer Corrigendum I, SI no 3
		Milestone		
		On Acceptance of Bid Process Management Report		
		On Acceptance of Inception Report		
		On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other submissions, test report audit report, compliance report, certificate, plan, manual and any other deliverable mentioned in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks		
		Percentage	Percentage	
		2.5% of contract Value	5% of contract value	
		2.5% of contract Value	2.5% of contract Value	
		8.5% of Contract Value per quarter.	2.5% of contract Value	
		On Acceptance of Bid Process Management Report	85% of Contract Value per quarter.	

Sl No	Reference Clause of RFP	Existing Clause of RFP		Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion										
		<table><tr><td>performed by each Experts.</td><td></td></tr><tr><td>On Acceptance of Final Completion report with CD</td><td>5% of Contract Value per quarter.</td></tr><tr><td colspan="2">•</td></tr></table>	performed by each Experts.		On Acceptance of Final Completion report with CD	5% of Contract Value per quarter.	•			<table><tr><td>in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts.</td><td></td></tr><tr><td>On Acceptance of Final Completion report with CD</td><td>5% of Contract Value</td></tr></table>	in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts.		On Acceptance of Final Completion report with CD	5% of Contract Value	
performed by each Experts.															
On Acceptance of Final Completion report with CD	5% of Contract Value per quarter.														
•															
in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts.															
On Acceptance of Final Completion report with CD	5% of Contract Value														
30.	Section 2. Instructions to Consultants and Data Sheet, (A) General Provisions-Pt.6.3	As an exception to the fore going ITC 6.1 and ITC 6.2 above: Joint Venture, association with other firms and engagement of Sub-consultant is not allowed.		We would like to request you to kindly allow Consortium/ JV of at least 2 Firms including the Lead Partner in order to be able to offer enhanced experience/ expertise and greater resource pool to the project.	Kindly refer Corrigendum I, SI no 4										
31.	Section 2. Instructions to Consultants and Data Sheet, (E) Data Sheet, Pt 14.1.2	Estimated input of Key Experts' time input: 68 person-months.		There seems to be a mismatch in the estimated time input of key experts as indicated in the Data Sheet and in the Terms of Reference. As per the Data Sheet it is 68-man months, whereas it is 143-man months as per the TOR. Kindly clarify and confirm.	Kindly refer Corrigendum I, SI no 2										
	Section 7. Terms of Reference, Pt 10	Staffing													
32.	Section 2. Instructions to Consultants and Data Sheet, (E) Data Sheet, Pt	Financial Proposal: To Be Submitted in the FINANCIAL FOLDER available in the eprocurement portal under the RFP: (1) FIN-1 (2) FIN-2		There is no format available for the Statement of Undertaking in the BOQ provided for the financial proposal.	Kindly refer to Corrigendum-I, SI no 10. The Bidder shall submit the Statement of Undertaking in										

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
	10.1	(3) FIN-3 (4) FIN-4 (5) Statement of Undertaking	Kindly inform where should we provide the same and if any format can be provided for it.	Technical Proposal to meet the requirement of ITB/BDS 10.2
33.	Section 2. Instructions to Consultants (E) Data Sheet, Pt. 17.7 and 17.9	The Proposals must be submitted no later than: Date: 17th August, 2021 Time: 14:00 hours IST	Considering the magnitude and complexity of the proposal, we request you to kindly extend the submission date by another 15 days to enable us to prepare a competitive and technically-responsive proposal.	Kindly refer Corrigendum I, Sl no 11.
34.	Section 2. Instructions to Consultants (E) Data Sheet, Pt. 21.1, Part A: Mandatory Criteria: Pt. 3	The firm should have completed in last 5 years at least 5(five) similar technical support consultancy services in any sector out of which: 1(one) should be in the water/marine sector. 1(one) should be externally aided project in India.	Considering technical support consultancies are usually long-term assignments, we request you to kindly consider competed as well as ongoing assignments in this criterion.	No Changes in the document. However, if the initial contract duration is completed and there is an extension of Contract due to additional scope, a proof of document to such affect shall be submitted in the proposal.
35.	Section 2. Instructions to Consultants (E) Data Sheet, Pt. 21.1, Part A: Mandatory Criteria: Pt 4	The firm should have experiences in last 5 years in providing technical support Service for at least 1 activities involving construction of: 1. Jetty in river/sea or a bridge in river. And 2. Civil works of Jetty/bridge involving minimum 1200 mm diameter or equivalent area piles in marine / river conditions.	1. We request you to also consider experience of consultants in providing technical support service for construction of similar structures such as embankments etc. 2. Since TSSC professionals will be the key drivers for this project, therefore we feel that such specific requirements in terms of relevant experience should be assessed in the CVs of the proposed experts rather than evaluating the same in the company's credentials	No changes in the documents

056

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion								
36.	Section 7. Terms of Reference, Pt 7.8 III. Special Conditions of Contract, Pt 14.1	However, for TSSC, the project duration considered as 24 Months which includes bid process management prior to award of contractor. The time period shall be Thirty (30) months from the commencement of services.	Kindly confirm the duration of the assignment.	Refer Corrigendum I, Sl no 1								
37.	Section 7. Terms of Reference, Pt 10	TSSC must provide CVs of both Key Experts and Non- Key Experts in their Technical Proposal.	Since there are no marks assigned to the CVs of non-key experts (As per Data Sheet Pt 21.1 Part B), therefore we request you to kindly allow us to provide the CVs of non-key experts after the award of contract and not at the proposal stage.	No Changes in the document.								
38.	III. Special Conditions of Contract, Pt. 41.2	<table><thead><tr><th>Milestone</th><th>Percentage</th></tr></thead><tbody><tr><td>On Acceptance of Bid Process Management Report</td><td>2.5% of contract Value</td></tr><tr><td>On Acceptance of Inception Report</td><td>2.5% of contract Value</td></tr><tr><td>On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other</td><td>8.5% of Contract Value per quarter.</td></tr></tbody></table>	Milestone	Percentage	On Acceptance of Bid Process Management Report	2.5% of contract Value	On Acceptance of Inception Report	2.5% of contract Value	On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other	8.5% of Contract Value per quarter.	<p>1. We feel that there is some error in the payment percentage against each milestone as the total payment percentage is coming out to be 83% only. We request you to kindly check and revise it accordingly.</p> <p>2. We understand that the Final Completion report is a one-time milestone to be submitted after completing the assignment, therefore we feel that there is some typing error in the payment percentage allocated to the same. We request you to kindly check and revise it accordingly.</p>	Kindly refer Corrigendum I, Sl no 3
Milestone	Percentage											
On Acceptance of Bid Process Management Report	2.5% of contract Value											
On Acceptance of Inception Report	2.5% of contract Value											
On Acceptance of Quarterly Progress Report subject to acceptance/completion of all other monthly and quarterly report/tasks and other	8.5% of Contract Value per quarter.											

355

SI No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
		<div> <div> submissions, test report audit report, compliance report, certificate, plan, manual and any other deliverable mentioned in the TOR during a quarter. Each invoice must also accompanied by a statement of key and non-key Expert deployments and tasks performed by each Experts. </div> <div> On Acceptance of Final Completion report with CD </div> <div> 5% of Contract Value per quarter. </div> </div>		
39.	Section Instructions to Consultants E. Data Sheet/ Part A: Mandatory Criteria: /SI no 3	<p>2. The firm should have completed in last 5 years atleast 5(five) similar technical support consultancy services in any sector out of which: 1(one) should be in the water/marine sector. 1(one) should be externally aided project in India.</p>	<p>We request you to consider Ongoing Projects which have achieved more than 85% physical progress for externally aided projects instead of only completed projects.</p> <p>Also we request you to externally aided projects executed during last 10 years instead of last 5 years.</p>	<p>No Changes in the document.</p> <p>However, if the initial contract duration is completed and there is an extension of Contract due to additional scope, a proof of document to such affect shall be submitted in the proposal.</p>
40.	Section Instructions to Consultants	<p>2. The firm should have experiences in last 5 years in providing technical support Service for at least 1 activities involving</p>	<p>We request you to consider Ongoing Projects which have achieved more than 85% physical progress for externally</p>	<p>No Changes in the document.</p>

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
	E. Data Sheet/ Part A: Mandatory Criteria: /SI no 4	construction of : 1. Jetty in river/sea or a bridge in river. And 2. Civil works of Jetty/bridge involving minimum 1200 mm diameter or equivalent area piles in marine / river conditions.	aided projects instead of only completed projects	However, if the initial contract duration is completed and there is an extension of Contract due to additional scope, a proof of document to such affect shall be submitted in the proposal.
41.	Section 2. Instructions to Consultants E. Data Sheet/ Part B	Minimum 5 similar assignment of technical support consultancy services in any sector - 1 point.	We assume similar assignments of technical support consultancy services also mean PMC or Construction Supervision Assignments. Kindly Confirm.	No changes in the document
42.	Technical/Experience Aspects:	iii) Minimum 1 similar assignment of technical support consultancy services in externally aided project in India in any sector executed in the last 5 years –1 point	We request you to consider Ongoing Projects which have achieved more than 85% physical progress for externally aided projects instead of only completed projects. Also we request you to externally aided projects executed during last 10 years instead of last 5 years.	No Changes in the document. However, if the initial contract duration is completed and there is an extension of Contract due to additional scope, a proof of document to such affect shall be submitted in the proposal.
43.		iv. Minimum of 1 nos. technical support service for activities involving construction of (executed in the last 5 years): 1. Jetty in river/sea or a bridge in river. And 2. Civil works of Jetty/bridge involving minimum 1200 mm diameter or equivalent area piles in marine / river conditions. : 1 point	We request you to consider Ongoing Projects which have achieved more than 85% physical progress for externally aided projects instead of only completed projects.	No Changes in the document. However, if the initial contract duration is completed and there is an extension of Contract due to additional scope, a proof of document to such affect shall be submitted in the proposal.

Sl No	Reference Clause of RFP	Existing Clause of RFP	Query/ Clarification/ Suggestion	Reply to Query/ Clarification/ Suggestion
44.	Section 2. Instructions to Consultants E. Data Sheet/ B. Preparation of Proposals/ 14.1.2	Estimated input of Key Experts' time-input: 68 person-months.	Kindly Confirm which shall supersede.	Kindly refer Corrigendum I, Sl no 1
	Section 7. Terms of Reference/ 10. Staffing	As per this clause Key Experts Time input is 143 person-months		
45.	Section 7. Terms of Reference/ PHASE – 1 7.1 Bid Process Management	Task 1: Bid process management for selection of Contractor(s) and execution of contract(s)	Task mentions scope related to only assisting for Pre-bid & Evaluation. In whose scope is preparing of Tender Documents & Inviting tenders?	The RFB is expected to be floated before the Proposal Due Date of TSSC. The successful bidder shall be informed about the remaining scope of work under Bid Process Management.
46.	Section 7. Terms of Reference/ PHASE – 2/ 7.2.3 Task 3: Design Review	Task 3: Design Review	Will there be a proof checking consultant for vetting the drawings from Structural safety point of view?	Contractor will submit the detailed design and drawings duly vetted by the Proof Consultant.

Deputy State Project Director


Assam Inland Water Transport Development Society

Annexure-III


Annexure-1


- NOTES
1. ALL DIMENSIONS ARE IN MM AND LEVELS ARE IN M.
 2. ONLY WRITTEN DIMENSIONS ARE TO BE FOLLOWED DRAWING SHOULD NOT BE SCALED UNDER ANY CIRCUMSTANCES.
 3. ALL MEASUREMENTS MUST BE CHECKED AND VERIFIED BY THE CONTRACTORS PRIOR TO EXECUTION OF WORK AT THE SITE.
 4. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT STRUCTURAL SERVICES, SECTIONS & DETAIL DRAWINGS.
 5. ARCHITECTURAL DRAWINGS ARE TO BE FOLLOWED FOR THE LOCATION OF ALL STRUCTURAL MEMBERS & MASONRY WALLS. FOR SIZES & REINFORCEMENT DETAILS OF STRUCTURAL MEMBERS, RELEVANT STRUCTURAL DRAWINGS ARE TO BE REFERRED.
 6. ANY DISCREPANCIES BETWEEN ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS MUST BE BROUGHT TO THE NOTICE OF HE ARCHITECTS IMMEDIATELY & PRIOR TO EXECUTION AT SITE.
 7. CO-ORDINATION WITH SERVICES SUCH AS PLUMBING & ELECTRICAL, ETC. IS THE RESPONSIBILITY OF THE CONTRACTORS.
 8. ALL MASONRY WALLS SHOULD BE ALIGNED WITH THE COLUMNS AS INDICATED ON THE PLAN, IRRESPECTIVE OF THE POSITION AS CALCULATED WITH THE DIMENSIONING.
 9. FOR DETAILS, REFER RELEVANT LARGE SCALE DETAIL DRGS. AS INDICATED.

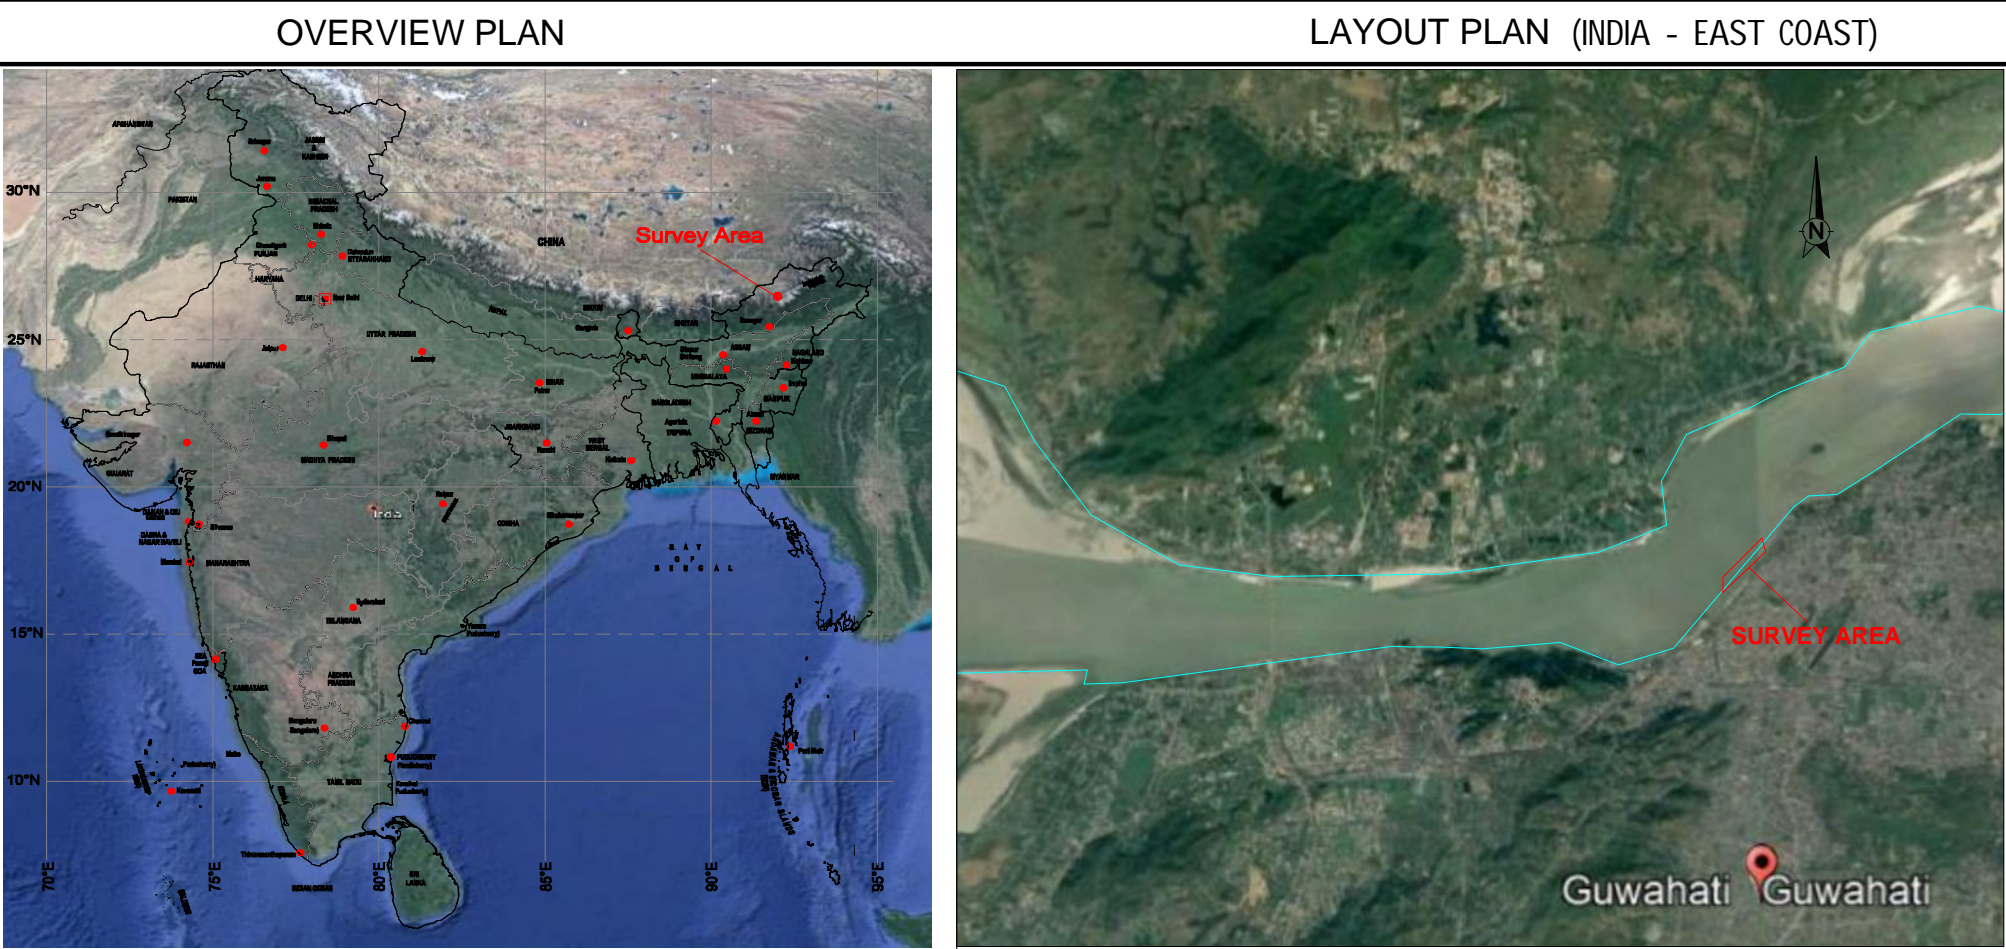


SCALE 0 1.50 3.75 7.50 15.0M



03	17-06-2021	DPR	ISSUED FOR APPROVAL			
02	24-05-2021	DPR	ISSUED FOR APPROVAL			
01	05-01-2021	DPR	ISSUED FOR APPROVAL			
00	14-06-2019	DPR	ISSUED FOR APPROVAL			
REV. No.	DATE	STAGE	DESCRIPTION	CIVIL	HM	E&M
				CHECKED		

CLIENT  ASSAM INLAND WATER TRANSPORT DEVELOPMENT SOCIETY (AIWTDs)

TRACTEBEL  **TRACTEBEL ENGINEERING PVT. LTD.**

	NAME	SIGN	PROJECT	DRAWING TITLE		
DRAWN BY	R S		PREPARATION OF DPR, FEED AND TENDER DESIGN FOR DEVELOPMENT OF FERRY SERVICES IN ASSAM			
CHECKED BY	M V H					
APPROVED BY	G R			GUWAHATI GATEWAY GHAT TERMINAL BUILDING SITE LEVEL LAYOUT PLAN		
DATE:-	17-06-2021		DRG NO.			
SHEET SIZE	A0	SCALE	1:150			
			P.013223-P-20318-201	REV.	03	SHEET 1 OF 1

This document and the information contained herein are the sole property of Tractebel engineering Pvt. Ltd. The reproduction, copying, distribution and utilization of this document, in full or in part, is prohibited without written consent. Offenders will be held liable for unauthorized use. All rights are reserved.

1 TERMINAL BUILDING SITE LEVEL LAYOUT PLAN Scale: 1:150
